



CLIENT
Midland County
804 N. Fort Worth St.
Midland, Texas 79701

PROJECT NO.
40263.22

04/24/2023 Permit Set
DATE DESCRIPTION

SCHEDULE


NTP: 2/5/24_ CONTRACT DURATION: 240d
ANTICIPATED COMPLETION: 01/2025
DAYS EXPENDED: 270_ %SCHED: 113%_

TRACKING ISSUES


REPLACE 2 SHOP CEILING FANS
TOUCH UP PAINT IN THE SHOP
FINISH LANDSCAPING

FINANCIALS

ORIGINAL CONTRACT VALUE: \$ 1,335,000
CHANGE ORDERS: \$ 36,460
Pending change orders: _____
CURRENT CONTRACT VALUE: \$ 1,371,460
BILLED TO DATE: \$ 1,366,459.93
PERCENT BILLED: 99%_

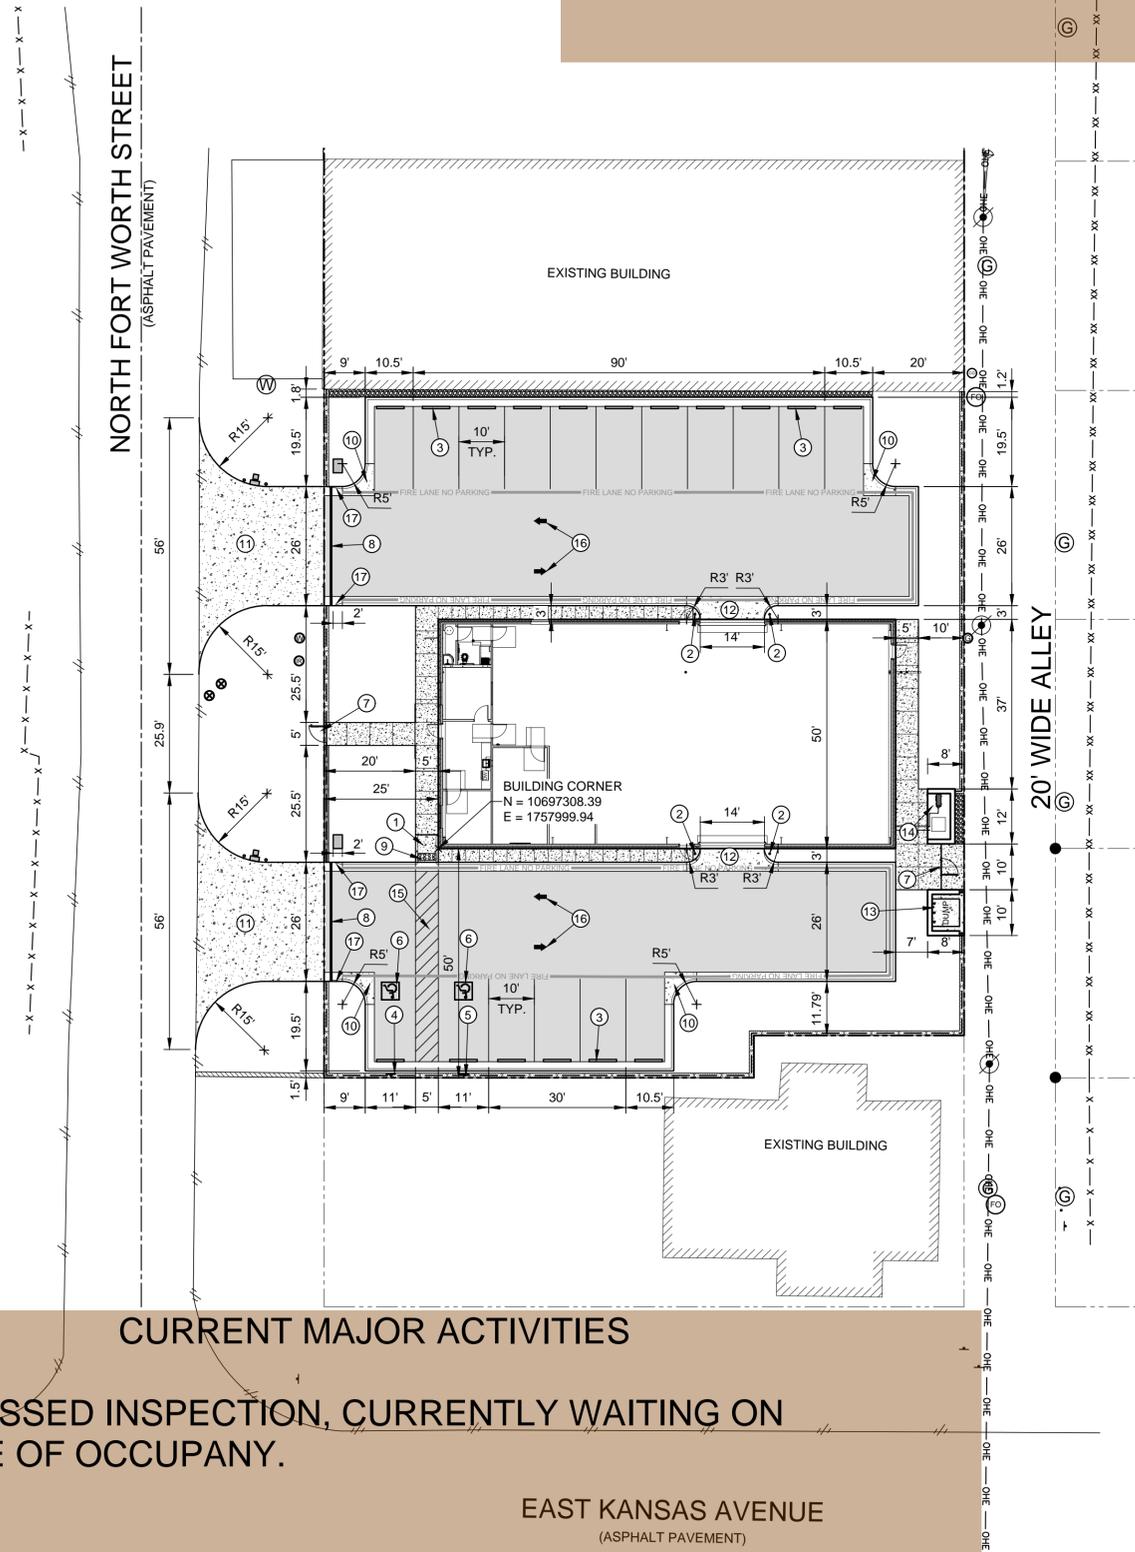

SITE PHOTO



Updated: 01/02/2025
